BILL NO. S-80-10-30

SPECIAL ORDINANCE NO. S-134-80

AN ORDINANCE approving Change Order No. 3 in connection with the St. Joseph Dam and Pump Station Additions.

BE IT ORDAINED BY THE COMMON COUNCIL OF THE CITY OF FORT WAYNE, INDIANA:

SECTION 1. That Change Order No. 3 to Shambaugh and Son, Inc. in connection with the St. Joseph Dam and Pump Station for:

the necessary additional labor, material and equipment to replace approximately 162 L.F. of top rail section

in the amount of $4,945.00, as set out in the specifications therefor, which are on file in the Office of the Board of Public Works and are by reference incorporated herein and made a part hereof, hereby in all things ratified, confirmed and approved.

SECTION 2. That this Ordinance shall be in full force and effect from and after its passage and approval by the Mayor.

COUNCILMAN

APPROVED AS TO FORM AND LEGALITY OCTOBER 10, 1980.

JOHN E. HOFFMAN
City Attorney

Read the first time in full and on motion by Burns, seconded by Stier, and duly adopted, read the second time by title and referred to the Committee City Plan (and the City Plan Commission for recommendation) and Public Hearing to be held after due legal notice, at the Council Chambers, City-County Building, Fort Wayne, Indiana, on ~~_____~~, the ~~_____~~ day of ~~_____~~, 19~~____~~, at ~~_____~~ o'clock ~~___~~ M.,E.S.T.

DATE: 10-14-80

Charles W. Westerman
CHARLES W. WESTERMAN
CITY CLERK

Read the third time in full and on motion by Burns, seconded by Stier, and duly adopted, placed on its passage. PASSED (~~LOST~~) by the following vote:

	AYES	NAYS	ABSTAINED	ABSENT	TO-WIT:
TOTAL VOTES	9				
BURNS	✓				
EISBART	✓				
GiaQUINTA	✓				
NUCKOLS	✓				
SCHMIDT, D.	✓				
SCHMIDT, V.	✓				
SCHOMBURG	✓				
STIER	✓				
TALARICO	✓				

DATE: 10-28-80

Charles W. Westerman
CHARLES W. WESTERMAN - CITY CLERK

Passed and adopted by the Common Council of the City of Fort Wayne, Indiana, as (~~ZONING MAP~~) (GENERAL) (ANNEXATION) (SPECIAL) (APPROPRIATION) ORDINANCE (~~RESOLUTION~~) No. S-134-80

on the 28th day of October, 19 80.

ATTEST:
Charles W. Westerman
CHARLES W. WESTERMAN - CITY CLERK

(SEAL)
Vivian G. Schmidt
PRESIDING OFFICER

Presented by me to the Mayor of the City of Fort Wayne, Indiana, on the 28th day of October, 19 80, at the hour of 2:30 o'clock P. M.,E.S.T.

Charles W. Westerman
CHARLES W. WESTERMAN - CITY CLERK

Approved and signed by me this 30th day of October 19 80, at the hour of 4 o'clock P M.,E.S.T.

WINFIELD C. MOSES, JR.
MAYOR

BILL NO. S-80-10-30

REPORT OF THE COMMITTEE ON CITY UTILITIES

WE, YOUR COMMITTEE ON CITY UTILITIES TO WHOM WAS REFERRED AN ORDINANCE approving Change Order No. 3 in connection with the St. Josèph Dam and Pump Station Additions

HAVE HAD SAID ORDINANCE UNDER CONSIDERATION AND BEG LEAVE TO REPORT BACK TO THE COMMON COUNCIL THAT SAID ORDINANCE DO PASS.

PAUL M. BURNS, CHAIRMAN

BEN EISBART, VICE CHAIRMAN

JOHN NUCKOLS

MARK GiaQUINTA

ROY SCHOMBURG

10-28-80
DATE

CONCURRED IN
CHARLES W. WESTERMAN, CITY CLERK

McNAMEE, PORTER & SEELEY
CONSULTING ENGINEERS
ANN ARBOR, MICHIGAN

69-169-19 9/17/80

OWNER: City of Fort Wayne, IN

CONTRACTOR: Shambaugh & Son, Inc.
137 Chambeau Road, P.O. Box 1287, Fort Wayne, IN 46805

CONTRACT NO. 77-W-3

TITLE: St. Joseph Dam & Pump Station Additions

CHANGE ORDER NO. 3

DATE: September 3, 1980

To the Contractor named above:

Under the above contract and upon approval of the Owner, we hereby direct you to furnish the necessary additional labor, material and equipment to:

Replace approximately 162 L.F. of top rail section, per attached Shambaugh & Son letter and sketch dated 8-22-80. ADD, $ 4,945.00

CURRENT CONTRACT AMOUNT	$880,523.90
THIS CHANGE ORDER, (ADD)	4,945.00
REVISED CONTRACT AMOUNT	$885,468.90

MCNAMEE, PORTER AND SEELEY

BY

Contract No.
City of Fort Wayne, IN
DATE:

ACCEPTED: DATE 9-10-80 CONTRACTOR: SHAMBAUGH & SON, INC.

* BY: James F Harvey

RECOMMENDED: DATE CITY ENGINEER

DATE 9/16/80 DIRECTOR OF WATER RESOURCES DIV. Philip R. Fuller

APPROVED & ADOPTED DATE 9/17/80 BOARD OF PUBLIC WORKS

BY (Chairman)

ATTEST: Sandra E Kennedy
Clerk Board of Public Works

* Qualified By our letter of Sept. 10, 1980 J.F.H.

DISTRIBUTION:
City - 2
Contractor - 1
MP&S - 1
Res. Engr. - 2
Glen Patrick - 1 (info.)
File - 1
ADK - 1

Shambaugh & Son INC.

MECHANICAL • ELECTRICAL • FIRE PROTECTION • WASTE WATER

137 Chambeau Road • P.O. Box 1287 • Fort Wayne, Indiana 46801 • Phone (219) 484-0741

August 22, 1980

McNamee, Porter & Seeley
3131 South State Street
Ann Arbor, Michigan 48104

Attention: John Oyer

Reference: City of Ft. Wayne, Indiana St. Joe Dam & Pump Station
Contract 77-W-3, Our No. 6273-X1, C.R. #5

Gentlemen:

At the request of Mr. Larder, we are pleased to quote the Lump Sum price of $4,945.00 to replace approximately 162 Lin. feet of Top Rail Section only of bridge, per attached sketch 8-22-80 and per following list of inclusions:

1. Demolition of 20 Lin. feet
2. Saw Cut ½" deep and square up existing ends
3. Clean, reposition existing Re-steel
4. Pour, finish, and patch approximately 162 feet of rail
5. Coat new concrete with standard gray Thoroseal And old portion of Rail
6. Clean up area

Heating of concrete is not included.

Subcontract quote (Indiana Construction Corp.)	$4,495.00
Contractors Fee	$ 450.00
Total	$4,945.00

Above price firm for 45 days, 15 days required to complete work. Order to proceed must be received by October 8, 1980

Extension of time of 51 calender days will be required to present contract.

Very truly yours,

SHAMBAUGH & SON, INC.

James Harvey, Manager
Water & Waste Division

JH:mk

encl. Sketch 8-22-80

RECEIVED
AUG 25 1980
McNAMEE, PORTER & SEELEY
BY

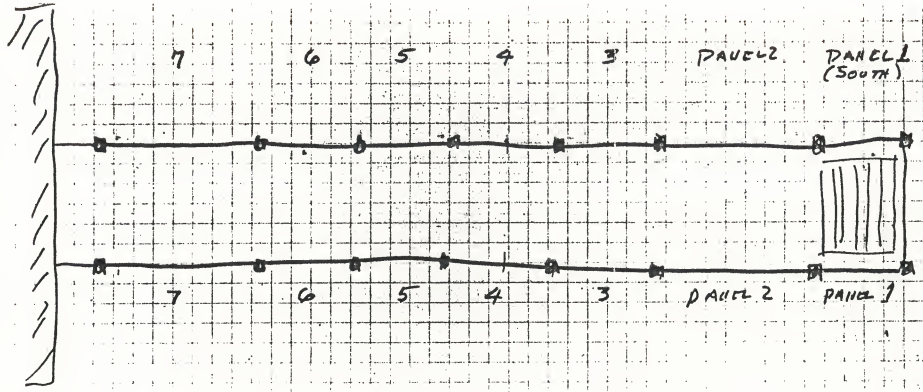

QUANTITY RAIL WORK (LIN. FT.)

	NEW RAIL No.	NEW RAIL So.	DEMOLITION EXIST No.	DEMOLITION EXIST So.
PANEL 1	12	16		
2	19	18		
3	2	8		6'
4	1	5		
5	12	5		
6	10	10		
7	44		14'	
TOTALS	162 L.F.		20 L.F.	

ST JOE DAM & P.S.
CONTRACT 77-W-3
BRIDGE TOP RAIL REPLACEMENT
SHAMBAUGH & SON INC.
JOB # 6273
SK B 22 80

Shambaugh & Son INC.

MECHANICAL • ELECTRICAL • FIRE PROTECTION • WASTE WATER

137 Chambeau Road • P.O Box 1287 • Fort Wayne, Indiana 46801 • Phone (219) 484-0741

Spetember 10, 1980

McNamee Porter & Seeley
3131 South State Street
Ann Arbor, Michigan 48104

ATTN: Mr. John Oyer

RE: St. Joe Dam & Pump Station
Contract 77-W-3
Our 6273 XI, C.R.#5
C.O.#3

Gentlemen:

We have received change order No. 3 and note that there are two discrepancies as regards our C.R.#5, dated August 22, 1980. One difference is the addition of Thoroseal Paint, top portion of rail only, of existing concrete. We agree that this is acceptable.

We also required a time extension to the contract of 51 calendar days providing we receive order to proceed by October 8, 1980. This requirement must remain a part of this change order, and we have signed the change order with this condition. We acknowledge that the work will be done concurrent with our pending 6273X C.R.#6 time extension.

Please keep in mind that this change order will have to be requested if cold weather protection is required.

Very truly yours,

SHAMBAUGH & SON, INC.

James Harvey
Manager, Water & Waste Division

JH/lf

3697

TITLE OF ORDINANCE Change Order No. 3, Contract No. 77-W-3, St. Joe Dam and Pump Station Additions

DEPARTMENT REQUESTING ORDINANCE BOARD OF PUBLIC WORKS

L-80-10-30

SYNOPSIS OF ORDINANCE Change Order No. 3, Contract No. 77-W-3, St. Joseph Dam and Pump Station Additions.. The necessary additional labor, material, and equipment to replace approximately 162 L.F. of top rail section.

Change Order Addition Cost $4,945.00, Revised Total of entire project will be $885.468.90.

(Change Order Attached)

EFFECT OF PASSAGE This Change Order request will replace approximately 162 LF of top rail section

EFFECT OF NON-PASSAGE Necessary Changes as Described as Above Cannot be Completed.

MONEY INVOLVED (DIRECT COSTS, EXPENDITURES, SAVINGS) $4,945.00 which will be paid for from the Water Department as part of their Filtration Plant Expansion Program.

ASSIGNED TO COMMITTEE City Utilities

sa
